


Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float	2005												2006											
									D	J	F	M	A	M	J	J	A	S	O	N	D	D	J	F	M	A	M	J	J	A	S	O

PROJECT MILESTONES								
PROJECT MILESTONE								
MILESTONES								
AAAA-0001	GMP ISSUED (start milestone)	0	0	22DEC04		22DEC04		0
AAAA-0010	NOTICE TO PROCEED FROM OWNER (start milestone)	0	0	04JAN05*		04JAN05		0
AAAA-0011	EXECUTE OWNER/CONTRACTOR CONTRACT(start mile)	0	0	21JAN05*		21JAN05		0
AAAA-0100	MOBILIZE CONSTRUCTION RESOURCES	10	10	28MAR05*	08APR05	28MAR05	08APR05	0
AAAA-0111	START CONSTRUCTION	1	1	11APR05	11APR05	11APR05	11APR05	0
XXBA-0380	BASEMENT SLAB ON GRADE COMPLETE (finish flag)	0	0		25JUL05		25JUL05	0
XX05-0330	5TH LEVEL STRUCTURAL DECK COMPLETE (finish flag)	0	0		29NOV05		29NOV05	0
STRL-0330	TOP OUT STRUCTURE SOUTH TOWER (finish flag)	0	0		20APR06		20APR06	0
STRL-0750	DRY-IN SOUTH TOWER (finish flag)	0	0		15JUN06		06OCT06	113
NTRL-0330	TOP OUT STRUCTURE NORTH TOWER (finish flag)	0	0		03JUL06		03JUL06	0
NTRL-0750	DRY-IN NORTH TOWER (finish flag)	0	0		28AUG06		06OCT06	39
XXXX-8888	TCO WALKS WITH CITY OF DENVER	30	30	01NOV06	14DEC06	01NOV06	14DEC06	0
ZZST-9995	SOUTH TOWER COMPLETE(finish milestone)- PHASE I	0	0		14DEC06		14DEC06	0
ZZZZ-9999	PROJECT COMPLETE (finish milestone) - PHASE II	0	0		11JAN07		11JAN07	0

PRECONSTRUCTION								
PRECONSTRUCTION								
PERMIT PROCESSING								
PCPP-0072	SUBMIT FOUNDATION SEWER USE/DRAIN PERMIT	15	15	16FEB05*	08MAR05	02MAY05	20MAY05	53
PCPP-0062	SUBMIT FOUNDATION PERMIT (thru 2nd floor)	20	20	16FEB05*	15MAR05	21FEB05	18MAR05	3
PCPP-0074	RE SUBMIT FOUNDATION SEWER/USE DRAIN PERMIT	5	5	09MAR05	15MAR05	23MAY05	27MAY05	53
PCPP-0064	RE SUBMIT FOUNDATION PERMIT (thru 2nd floor)	5	5	16MAR05	22MAR05	21MAR05	25MAR05	3
PCPP-0076	OBTAIN FOUNDATION SEWER USE/DRAIN PERMIT	10	10	16MAR05	29MAR05	31MAY05	13JUN05	53
PCPP-0066	OBTAIN FOUNDATION PERMIT (thru 2nd floor)	10	10	23MAR05	05APR05	28MAR05	08APR05	3
PCPP-0082	SUBMIT FULL BLDG SEWER USE/DRAIN PERMIT	20	20	27APR05*	24MAY05	20MAY05	17JUN05	17
PCPP-0092	SUBMIT FULL BUILDING PERMIT	25	25	27APR05*	01JUN05	27APR05	01JUN05	0
PCPP-0084	RE SUBMIT FULL BLDG SEWER/USE DRAIN PERMIT	10	10	25MAY05	08JUN05	20JUN05	01JUL05	17
PCPP-0094	RE SUBMIT FULL BUILDING PERMIT	10	10	02JUN05	15JUN05	02JUN05	15JUN05	0
PCPP-0086	OBTAIN FULL BLDG SEWER USE/DRAIN PERMIT	15	15	09JUN05	29JUN05	05JUL05	25JUL05	17
PCPP-0096	OBTAIN FULL BUILDING PERMIT	20	20	16JUN05	14JUL05	16JUN05	14JUL05	0

PRICING								
PCPR-0130	PREPARE SUB PRICING	30	30	04JAN05	14FEB05	23FEB05	05APR05	36
PCPR-0170	REVIEW BIDS/AWARD SUBCONTRACTS	10	10	15FEB05	28FEB05	06APR05	19APR05	36

ACTIVITIES AFFECTING ALL FLOORS								
ALL FLOORS								
ALL FLOORS								
AFAF-0112	TOWER CRANE FOR SOUTH TOWER	336	336	16MAY05*	16APR06	16MAY05	16APR06	0
AFAF-0111	TOWER CRANE FOR NORTH TOWER	420	420	24MAY05*	17JUL06	24MAY05	17JUL06	0

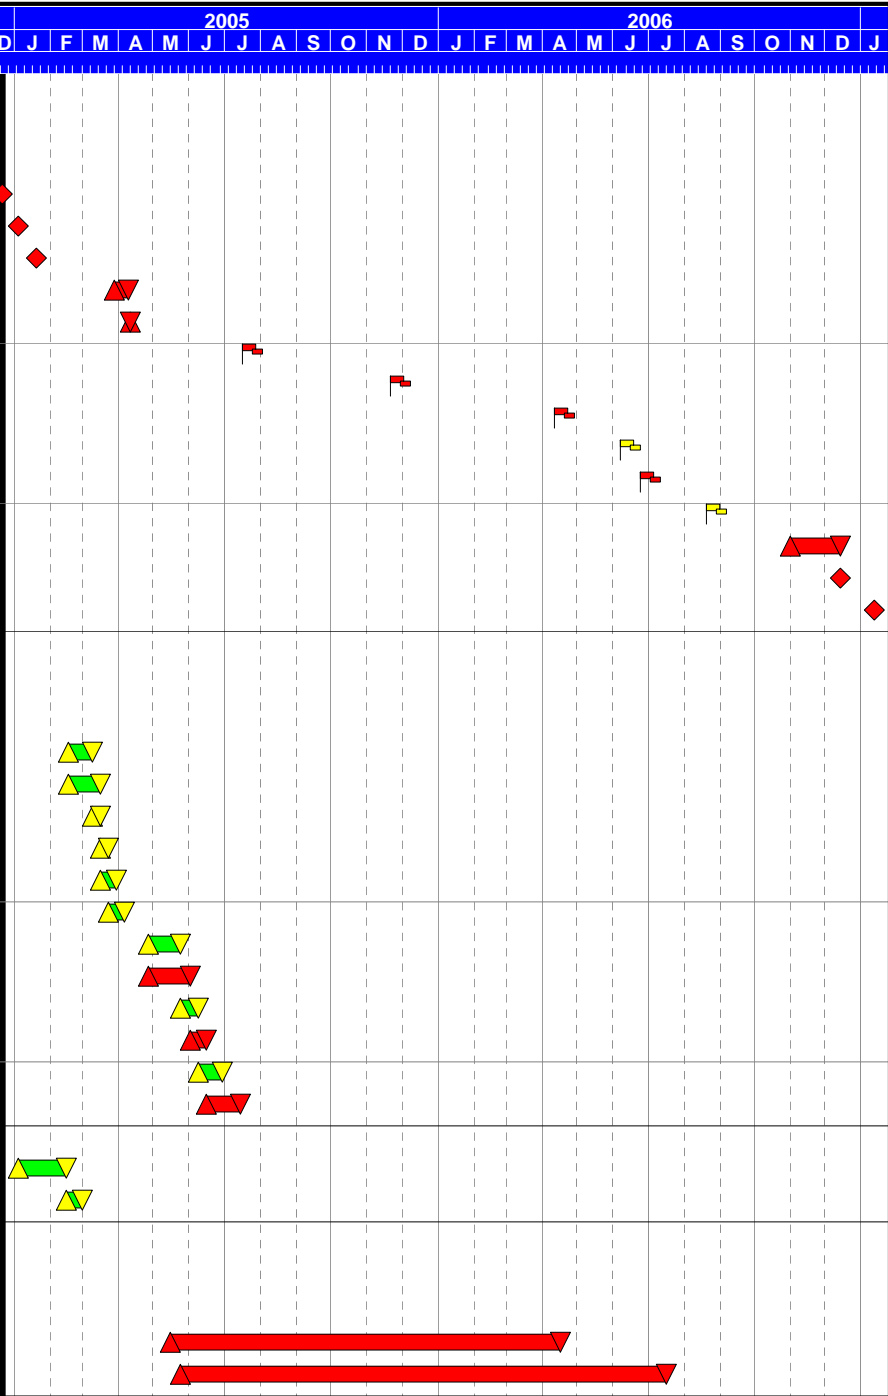

Start Date 06DEC04
 Finish Date 11JAN07
 Data Date 22DEC04
 Run Date 29JAN08 13:49

Date	Revision	Checked	Approved

