Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
PROJECT MILESTONES							
MILESTONES/FLAGS/KEY ACTIVITIES							
PROJECT MILESTONES							
AAAA-0010	START NETWORK ANALYSIS (start milestone)	0	03MAY04A		03MAY04A		
AAAA-0100	MOBILIZE CONSTRUCTION RESOURCES	10	15JUN04	28JUN04	01JUL04	14JUL04	12
AAAA-0110	LOAN DECISION MADE	0	13SEP04*		13SEP04		0
XXTCS-0188	MAINTAIN SOUTH TOWER CRANE (hammock)	324*	04OCT04	23AUG05	27SEP04	03NOV05	-7
XXTCN-0188	MAINTAIN NORTH TOWER CRANE (hammock)	281*	12OCT04	19JUL05	04OCT04	19JUL05	-8
ZZZSW-0290	SITEWORK COMPLETE (finish milestone)	0		12OCT06		15DEC06	64
ZZZDT-9998	DIAGNOSTIC/TREATMENT COMPLETE (finish milestone)	0		04DEC06		15DEC06	11
ZZZPT-9998	PATIENT TOWER COMPLETE (finish milestone)	0		11JAN07		15DEC06	-27
ZZZZZ-9999	PROJECT COMPLETE (finish milestone)	0		11JAN07		15DEC06*	-27
DIAGNOSTIC/TREATMENT MILESTONES							
AAADT-0730	START EXT SKIN DIAGNOSTIC/TREATMENT(start flag)	0	15JUN04		15JUN04		0
XXXDT-0330	COMPLETE STRUC CONC FOR DIAGNOSTIC/TREATMNT (ff)	0		11JAN07		11JAN07	0
XXXDT-0750	DIAGNOSTIC/TREATMENT AREA DRIED-IN (finish flag)	0		11JAN07		11JAN07	0
PATIENT TOWER MILESTONES							
AAAPT-0730	START EXT SKIN PATIENT TOWER (start flag)	0	15JUN04		15JUN04		0
XXXPT-0330	COMPLETE STRUC CONC FOR PATIENT TOWER (ff)	0		11JAN07		11JAN07	0
XXXPT-0750	PATIENT TOWER DRIED-IN (finish flag)	0		11JAN07		11JAN07	0
SITEWORK MILESTONES							
AAASW-0290	START HARDSCAPING/LANDSCAPING (start flag)	0	04OCT04		19MAY06		592
XXXSW-0290	HARDSCAPE/LANDSCAPE COMPLETE (finish flag)	0		12OCT06		15DEC06	64
CENTRAL UTILITY PLANT ACTIVITIES							
CENTRAL PLANT MILESTONES							
ZZCUP-9998	CENTRAL UTILITY PLANT COMPLETE(finish milestone)	0		15FEB06		15FEB06	0

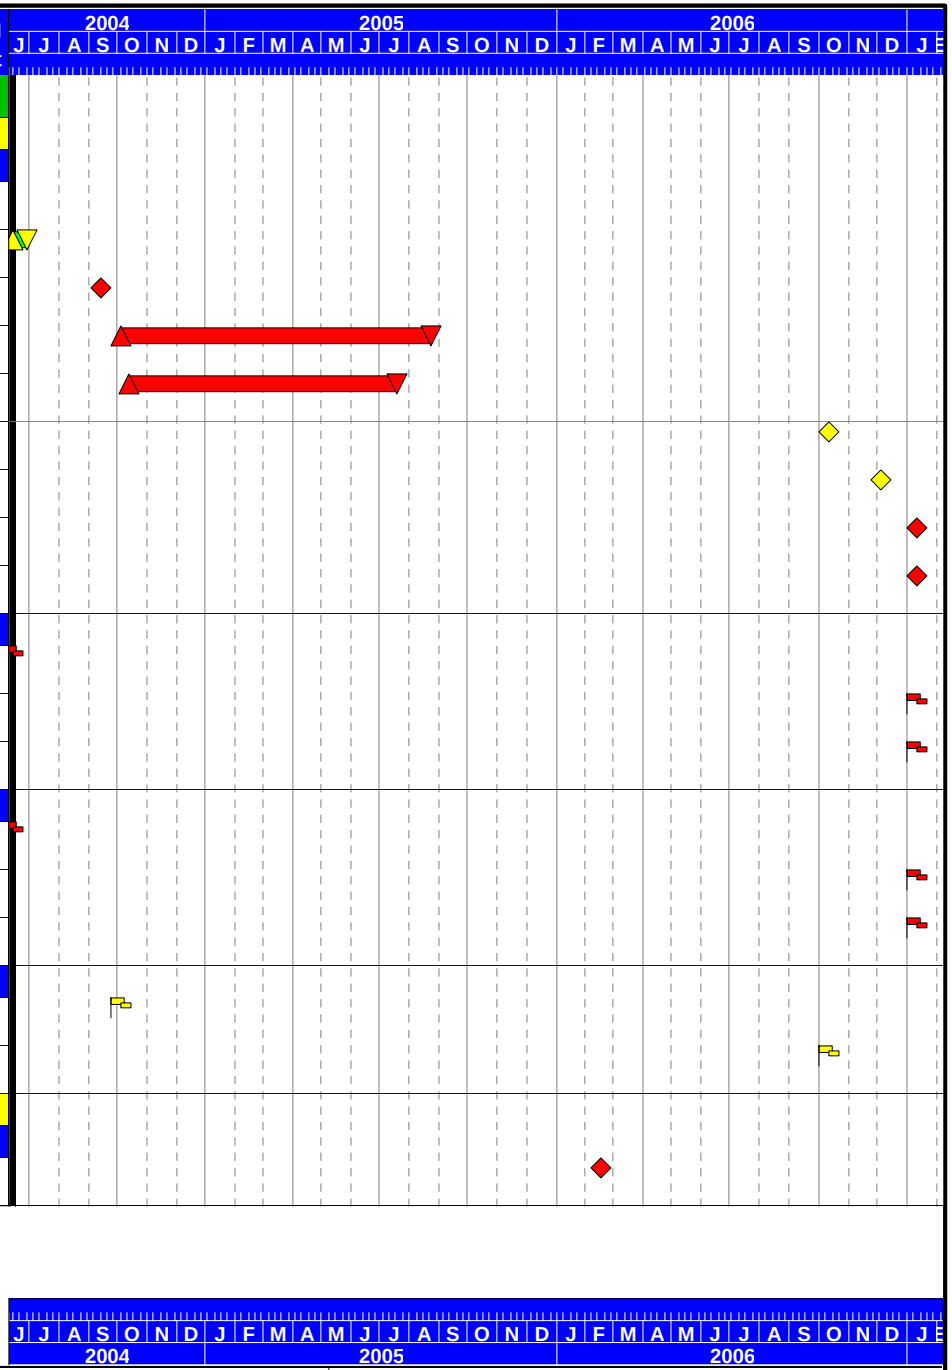

Start Date	01APR04
Finish Date	11JAN07
Data Date	15JUN04
Run Date	11FEB08 13:26

© Primavera Systems, Inc.

MCBL

SCHEDULING CONSULTANTS, LTD.
BASELINE SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
DESIGN ACTIVITIES							
DESIGN/SYSTEMS ENGINEERING							
DESIGN ACTIVITIES							
DEDES-0100	CONSTRUCTION DOCUMENTS COMPLETE	30	15JUN04	26JUL04	15DEC04	27JAN05	128
PRECONSTRUCTION ACTIVITIES							
PRE-CONSTRUCTION/PRICING/CONTRACT AWARD							
PRE-CONSTRUCTION/SUBCONTRACTOR PRICING							
PRPRC-0120	SUBCONTRACTOR PRICING (balance)	40	13SEP04	05NOV04	28JAN05	24MAR05	95
PRPRC-0122	REVIEW/AWARD SUBCONTRACTS (balance)	45	08NOV04	13JAN05	25MAR05	26MAY05	95
PERMIT PROCESSING							
PRE-CONSTRUCTION/SUBCONTRACTOR PRICING							
PRPER-0237	SUBMIT/OBTAIN FOOTING/FOUNDATION PERMIT	33*	02JUN04A	16JUL04	02JUN04A	14JUL04	-2
PRPER-1602	SUBMIT/OBTAIN UNDERGROUND ELEC SITE PERMIT	15	27SEP04*	15OCT04	05MAY06	25MAY06	409
PROCUREMENT ACTIVITIES							
PREPARE/SUBMIT SHOP DRAWINGS/SUBMITTALS							
PREPARE & SUBMIT FOR APPROVAL SHOP DRAWINGS							
POPSS-1510	PREP/SUBMIT HVAC TERMINAL BOX SUBMITTALS	10	13SEP04	24SEP04	09DEC04	22DEC04	61
POPSS-1520	PREP/SUBMIT CHILLER SUBMITTALS	10	13SEP04	24SEP04	19APR05	02MAY05	152
POPSS-1515	PREP/SUBMIT BOILER SUBMITTALS	10	13SEP04	24SEP04	19MAY05	02JUN05	174
POPSS-1600	PREP/SUBMIT SWITCHGEAR SUBMITTALS	10	13SEP04	24SEP04	31MAY05	13JUN05	181
POPSS-1525	PREP/SUBMIT RTU SUBMITTALS	10	13SEP04	24SEP04	21DEC05	04JAN06	323
POPSS-0440	PREP/SUBMIT EXT STONE SUBMITTALS	10	14JAN05	27JAN05	27MAY05	10JUN05	95
POPSS-0930	PREP/SUBMIT TERAZZO FLOORING SUBMITTALS	10	14JAN05	27JAN05	09SEP05	22SEP05	167
POPSS-1400	PREP/SUBMIT HYDROLIC ELEVATOR SUBMITTALS	10	14JAN05	27JAN05	04NOV05	17NOV05	207
POPSS-1100	PREP/SUBMIT KITCHEN EQUIPMENT SUBMITTALS	10	14JAN05	27JAN05	16NOV05	01DEC05	215
POPSS-0850	PREP/SUBMIT DOOR/HARDWARE SUBMITTALS	10	14JAN05	27JAN05	22NOV05	07DEC05	219
POPSS-0442	PREP/SUBMIT EXT MASONRY SUBMITTALS	10	14JAN05	27JAN05	28NOV05	09DEC05	221
POPSS-1410	PREP/SUBMIT TRACTION ELEVATOR SUBMITTALS	10	14JAN05	27JAN05	29NOV05	12DEC05	222

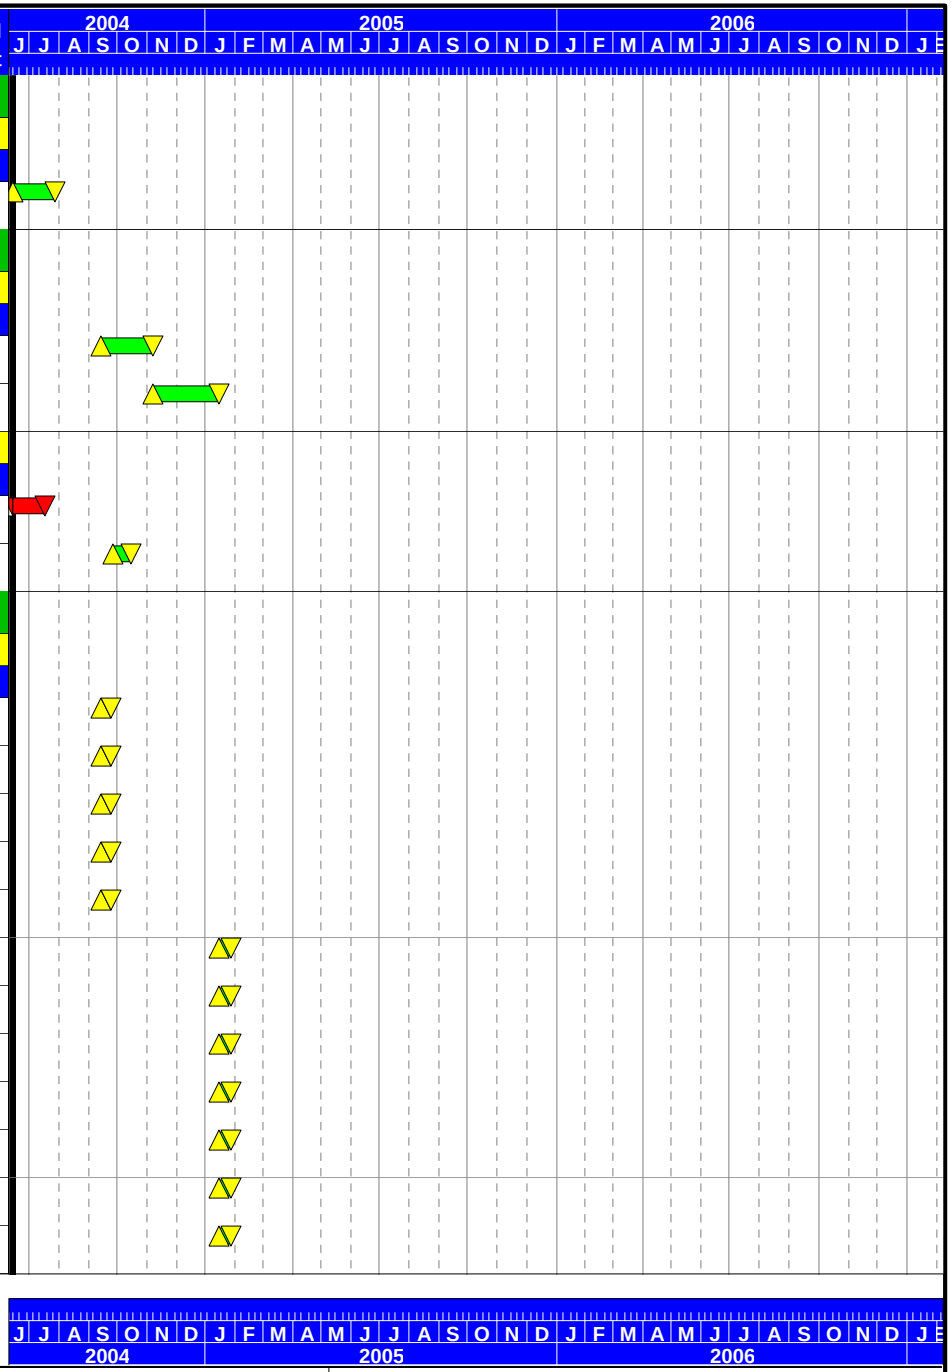

Start Date	01APR04
Finish Date	11JAN07
Data Date	15JUN04
Run Date	11FEB08 13:26

© Primavera Systems, Inc.

MCBL

SCHEDULING CONSULTANTS, LTD.
BASELINE SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
PREPARE & SUBMIT FOR APPROVAL SHOP DRAWINGS							
POPSS-0610	PREP/SUBMIT CABINETS/CASEWORK SUBMITTALS	20	14JAN05	10FEB05	15MAR06	11APR06	297
POPSS-0820	PREP/SUBMIT AUTOMATIC DOOR SUBMITTALS	10	14JAN05	27JAN05	24APR06	05MAY06	325
POPSS-0960	PREP/SUBMIT CARPET SUBMITTALS	10	14JAN05	27JAN05	01MAY06	12MAY06	330
POPSS-1620	PREP/SUBMIT DECORATIVE LIGHT FIXTURE SUBMITTALS	10	14JAN05	27JAN05	21AUG06	01SEP06	408
APPROVE SHOP DRAWINGS/SUBMITTALS							
APPROVE SHOP DWGS/PRODUCT DATA SUBMITTALS							
POAPP-1510	APPROVE HVAC TERMINAL BOX SUBMITTALS	10	27SEP04	08OCT04	23DEC04	07JAN05	61
POAPP-1520	APPROVE CHILLER SUBMITTALS	10	27SEP04	08OCT04	03MAY05	16MAY05	152
POAPP-1515	APPROVE BOILER SUBMITTALS	10	27SEP04	08OCT04	03JUN05	16JUN05	174
POAPP-1600	APPROVE SWITCHGEAR SUBMITTALS	10	27SEP04	08OCT04	14JUN05	27JUN05	181
POAPP-1525	APPROVE RTU SUBMITTALS	10	27SEP04	08OCT04	05JAN06	18JAN06	323
POAPP-0440	APPROVE EXT STONE SUBMITTALS	10	28JAN05	10FEB05	13JUN05	24JUN05	95
POAPP-0930	APPROVE TERAZZO FLOORING SUBMITTALS	10	28JAN05	10FEB05	23SEP05	06OCT05	167
POAPP-1400	APPROVE HYDROLIC ELEVATOR SUBMITTALS	10	28JAN05	10FEB05	18NOV05	05DEC05	207
POAPP-1100	APPROVE KITCHEN EQUIPMENT SUBMITTALS	10	28JAN05	10FEB05	02DEC05	15DEC05	215
POAPP-0850	APPROVE DOOR/HARDWARE SUBMITTALS	10	28JAN05	10FEB05	08DEC05	21DEC05	219
POAPP-0442	APPROVE EXT MASONRY SUBMITTALS	10	28JAN05	10FEB05	12DEC05	26DEC05	221
POAPP-1410	APPROVE TRACTION ELEVATOR SUBMITTALS	10	28JAN05	10FEB05	13DEC05	27DEC05	222
POAPP-0820	APPROVE AUTOMATIC DOOR SUBMITTALS	10	28JAN05	10FEB05	08MAY06	19MAY06	325
POAPP-0960	APPROVE CARPET SUBMITTALS	10	28JAN05	10FEB05	15MAY06	26MAY06	330
POAPP-1620	APPROVE DECORATIVE LIGHT FIXTURE SUBMITTALS	10	28JAN05	10FEB05	05SEP06	18SEP06	408
POAPP-0610	APPROVE CABINETS/CASEWORK SUBMITTALS	10	11FEB05	24FEB05	12APR06	25APR06	297
FABRICATE/DELIVER MATERIALS/EQUIPMENT							
FABRICATE/DELIVER MATERIALS/EQUIPMENT							
POFAB-1510	FAB/DELIVER HVAC TERMINAL BOXES	30	11OCT04	19NOV04	10JAN05	18FEB05	61
POFAB-1520	FAB/DELIVER CHILLERS	60	11OCT04	06JAN05	17MAY05	10AUG05	152

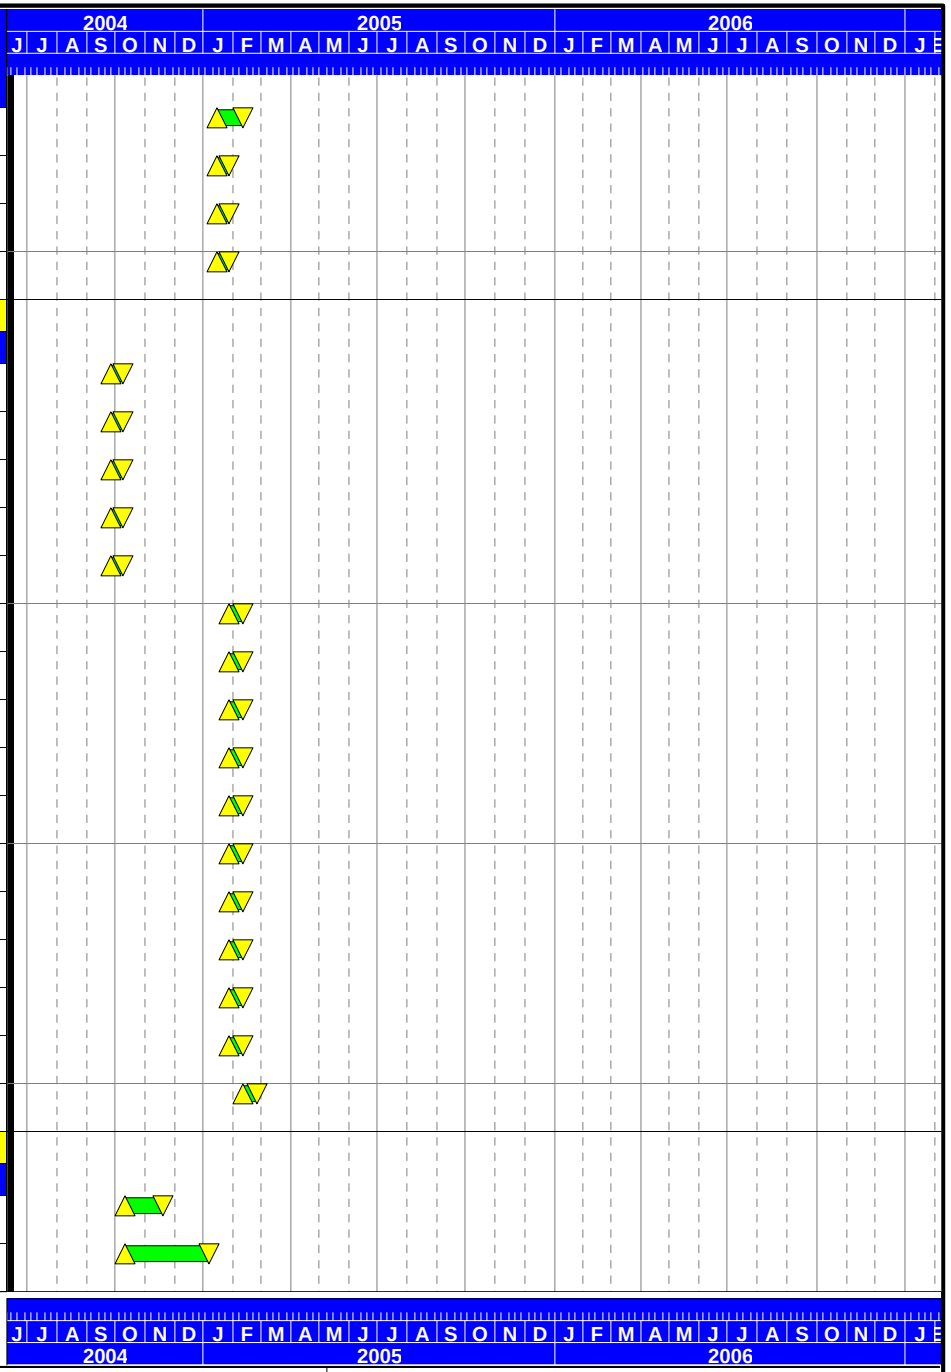

Start Date	01APR04
Finish Date	11JAN07
Data Date	15JUN04
Run Date	11FEB08 13:26

© Primavera Systems, Inc.

MCBL

SCHEDULING CONSULTANTS, LTD.
BASELINE SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
FABRICATE/DELIVER MATERIALS/EQUIPMENT							
POFAB-1515	FAB/DELIVER BOILERS	60	11OCT04	06JAN05	17JUN05	12SEP05	174
POFAB-1600	FAB/DELIVER SWITCHGEAR	65	11OCT04	13JAN05	28JUN05	28SEP05	181
POFAB-1525	FAB/DELIVER RTUS	45	11OCT04	14DEC04	19JAN06	22MAR06	323
POFAB-0440	FAB/DELIVER EXTERIOR STONE	35	11FEB05	31MAR05	27JUN05	15AUG05	95
POFAB-0930	FAB/DELIVER TERAZZO MATERIALS	20	11FEB05	10MAR05	07OCT05	03NOV05	167
POFAB-1400	FAB/DELIVER HYDROLIC ELEVATORS	60	11FEB05	05MAY05	06DEC05	28FEB06	207
POFAB-1100	FAB/DELIVER KITCHEN EQUIPMENT	65	11FEB05	12MAY05	16DEC05	17MAR06	215
POFAB-0850	FAB/DELIVER DOOR/HARDWARE	30	11FEB05	24MAR05	22DEC05	02FEB06	219
POFAB-0442	FAB/DELIVER EXTERIOR MASONRY	15	11FEB05	03MAR05	27DEC05	16JAN06	221
POFAB-1410	FAB/DELIVER TRACTION ELEVATORS	60	11FEB05	05MAY05	28DEC05	21MAR06	222
POFAB-0820	FAB/DELIVER AUTOMATIC DOORS	35	11FEB05	31MAR05	22MAY06	11JUL06	325
POFAB-0960	FAB/DELIVER CARPET	30	11FEB05	24MAR05	30MAY06	11JUL06	330
POFAB-1620	FAB/DELIVER DECORATIVE LIGHT FIXTURES	30	11FEB05	24MAR05	19SEP06	30OCT06	408
POFAB-0610	FAB/DELIVER CABINETS/CASEWORK	30	25FEB05	07APR05	26APR06	07JUN06	297
SITEWORK ACTIVITIES							
BUILDING PAD & INFASTRUCTURE							
SITEWORK							
SWBPI-0220	OVERLOT GRADING - BLDG PAD/INFASTR	35	03MAY04A	24JUN04	03MAY04A	26JAN06	348
SWBPI-0225	EXCAVATE WEST DETENTION POND - BLDG PAD/INFASTR	20	03MAY04A	26MAY04A	03MAY04A	26MAY04A	
SWBPI-0226	EXCAVATE EAST DETENTION POND - BLDG PAD/INFASTR	20	03MAY04A	26MAY04A	03MAY04A	26MAY04A	
SWBPI-0230	INSTALL SANITARY SEWER(line A)- BLDG PAD/INFASTR	20	15JUN04	14JUL04	14FEB06	20MAR06	365
SWBPI-0231	STORM DRAINS (lines D,J,I) - BLDG PAD/INFASTR	10	15JUN04	29JUN04	04MAY06	18MAY06	410
SWBPI-0241	INSTALL STORM DRAIN (line H) - BLDG PAD/INFASTR	5	15JUN04	21JUN04	11MAY06	18MAY06	415
SWBPI-0232	INSTALL SANITARY SEWER(line B)- BLDG PAD/INFASTR	20	25JUN04	26JUL04	27JAN06	02MAR06	348
SWBPI-0239	INSTALL STORM DRAIN (line C) - BLDG PAD/INFASTR	20	25JUN04	26JUL04	21MAR06	24APR06	378

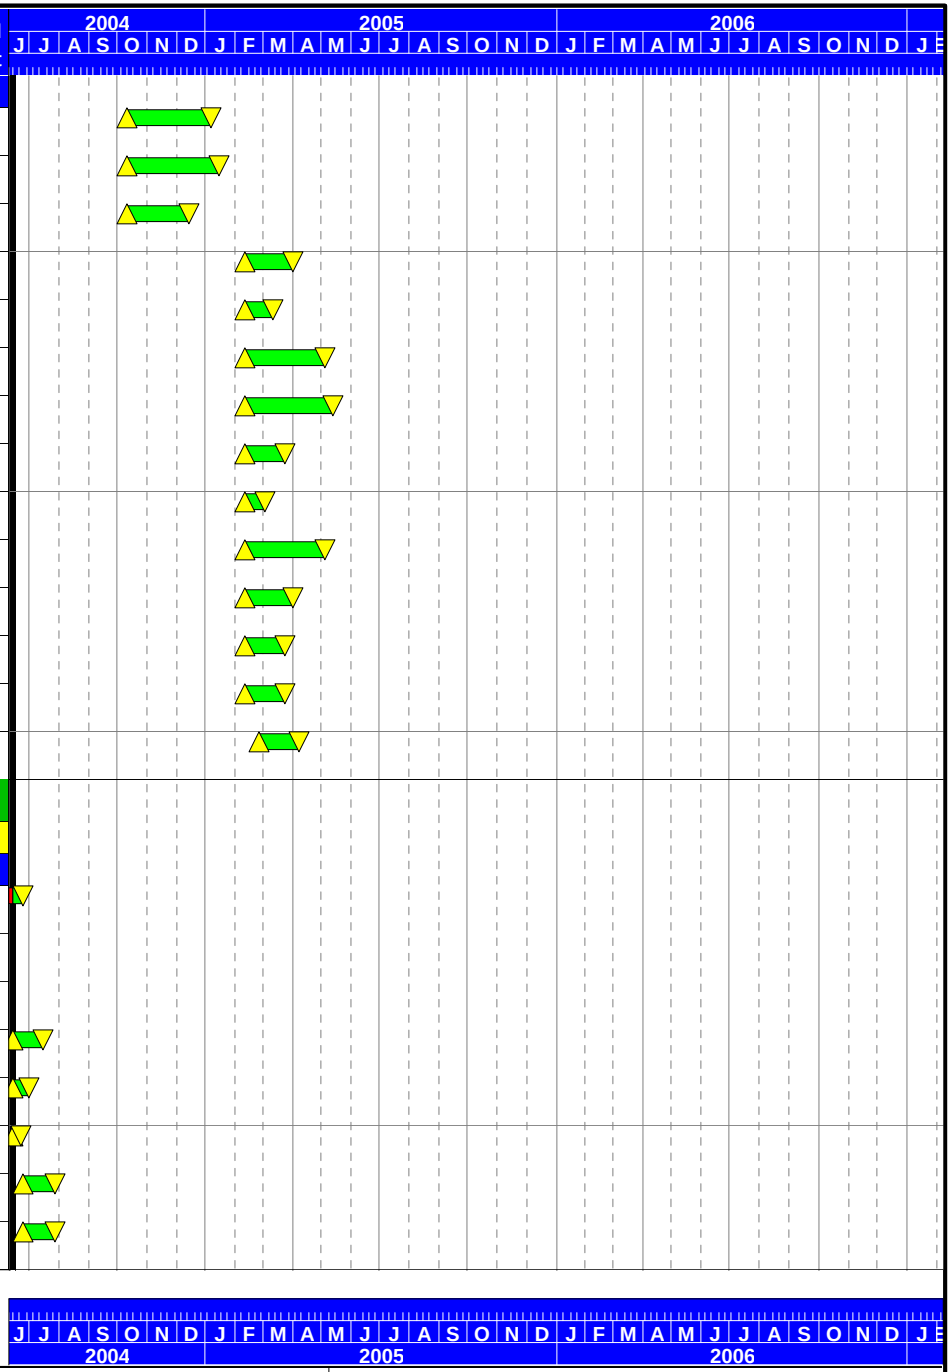

Start Date	01APR04
Finish Date	11JAN07
Data Date	15JUN04
Run Date	11FEB08 13:26

© Primavera Systems, Inc.

MCBL

SCHEDULING CONSULTANTS, LTD.
BASELINE SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
SITEWORK							
SWBPI-0228	INSTALL STORM DRAIN (line B) - BLDG PAD/INFASTR	10	25JUN04	09JUL04	07APR06	24APR06	388
SWBPI-0229	INSTALL STORM DRAIN (line A) - BLDG PAD/INFASTR	10	25JUN04	09JUL04	07APR06	24APR06	388
SWBPI-0244	INSTALL WATER MAIN (line A) - BLDG PAD INFASTR	15	12JUL04	02AUG04	25APR06	18MAY06	388
SWBPI-0237	INSTALL STORM DRAIN (line F) - BLDG PAD/INFASTR	20	15JUL04	13AUG04	21MAR06	24APR06	365
SWBPI-0234	INSTALL STORM DRAIN (line K) - BLDG PAD/INFASTR	15	27JUL04	17AUG04	03MAR06	28MAR06	348
SWBPI-0242	INSTALL WATER MAIN (line E) - BLDG PAD INFASTR	15	27JUL04	17AUG04	25APR06	18MAY06	378
SWBPI-0246	INSTALL WATER MAIN (line D) - BLDG PAD INFASTR	15	27JUL04	17AUG04	25APR06	18MAY06	378
SWBPI-0240	INSTALL WATER MAIN (line C) - BLDG PAD INFASTR	15	16AUG04	03SEP04	25APR06	18MAY06	365
SWBPI-0235	INSTALL STORM DRAIN (line E) - BLDG PAD/INFASTR	20	18AUG04	17SEP04	30MAR06	02MAY06	348
SWBPI-0236	INSTALL STORM DRAIN (line G) - BLDG PAD/INFASTR	10	20SEP04	01OCT04	04MAY06	18MAY06	348
PARKING LOT ONE							
SITEWORK							
SWPL1-0231	FINE GRADE FOR LANDSCAPE/HARDSCAPE- SW PKG ONE	3	27SEP04*	29SEP04	28JUN06	30JUN06	378
SWPL1-1610	R-I SITE LIGHTING - SW PKG ONE	7	30SEP04	11OCT04	03JUL06	13JUL06	378
SWPL1-0225	INSTALL IRRIGATION SLEEVES - SW PKG ONE	3	30SEP04	04OCT04	02AUG06	04AUG06	397
SWPL1-0216	INSTALL LIGHT POLE BASES - SW PKG ONE	4	05OCT04	11OCT04	22SEP06	28SEP06	428
SWPL1-0228	FORM/PLACE/FINISH CURB&GUTTER - SW PKG ONE	10	12OCT04	26OCT04	03AUG06	17AUG06	391
SWPL1-1605	R-I ELECTRICAL PRIMARY FEEDERS - SW PKG ONE	4	18OCT04*	22OCT04	25AUG06	30AUG06	402
SWPL1-0230	FINE GRADE/COMP SUBGRADE (PKG)- SW PKG ONE	3	28OCT04	01NOV04	18AUG06	22AUG06	391
SWPL1-0268	PLACE ASPHALT (first lift) - SW PKG ONE	3	02NOV04	04NOV04	23AUG06	25AUG06	253
SWPL1-0233	FORM/PLACE FINISH SIDEWALKS - SW PKG ONE	5	01MAY06*	08MAY06	21AUG06	25AUG06	71
SWPL1-0269	PLACE ASPHALT (final lift) - SW PKG ONE	3	03JUL06*	07JUL06	28AUG06	30AUG06	36
SWPL1-0288	INSTALL IRRIGATION SYSTEMS - SW PKG ONE	5	10JUL06	14JUL06	21SEP06	28SEP06	49
SWPL1-0277	STRIPE PARKING LOTS - SW PKG ONE	2	10JUL06	11JUL06	10OCT06	11OCT06	60
SWPL1-1620	INSTALL LIGHT POLES/FIXTURES - SW PKG ONE	2	10JUL06	11JUL06	10OCT06	11OCT06	60

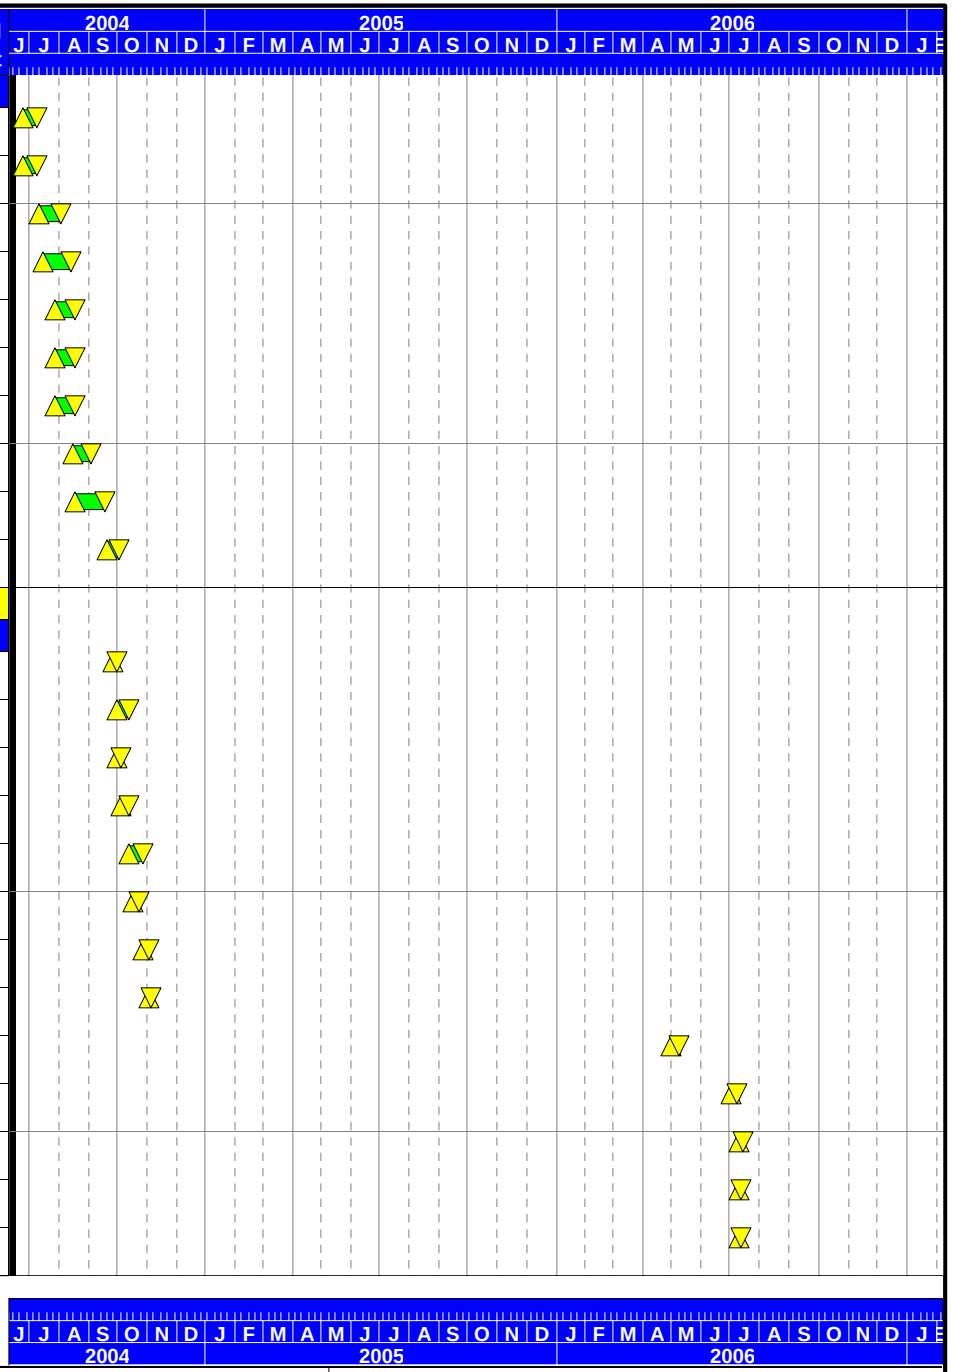

Start Date	01APR04
Finish Date	11JAN07
Data Date	15JUN04
Run Date	11FEB08 13:26

© Primavera Systems, Inc.

MCBL

SCHEDULING CONSULTANTS, LTD.
BASELINE SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA

Date	Revision	Checked	Approved
