Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
OVERALL MILESTONES/KEY DATES/NOTABLE ACTIVITIES								
PROJECT MILESTONES								
PROJECT MILESTONES/KEY DATES								
AAAA-0000	START NETWORK ANALYSIS	3	0	05OCT07		28NOV07		54
GMPR-0300	JE DUNN PREPARE/SUBMIT PRELIM SCHEDULE & GMP	3	68*	05OCT07	11DEC07	28NOV07	03FEB08	54
GMPR-0400	OWNER REVIEW/APPROVE GMP	3	7	12DEC07	18DEC07	04FEB08	10FEB08	54
AAAA-0100	MOBILIZE JE DUNN CONSTRUCTION RESOURCES	2	10	02JAN08*	15JAN08	28JAN08	08FEB08	18
AAAA-0150	START FNDTN WORK @ TUNNEL/HOTEL(start milestone)	3	0	21JAN08*		18APR08		88
ZZHT-0100	OVERALL DURATION FOR HOTEL (hammock)(cal days)	3	509*	21JAN08	12JUN09	18APR08	21SEP09	88
AAAA-0115	OWNER ISSUE NTP FOR CONSTRUCTION	3	0	11FEB08*		11FEB08		0
AAAA-0155	START FNDTN WORK @ CASINO/BOH (start milestone)	3	0	11FEB08*		11FEB08		0
ZZBH-0100	OVERALL DURATION FOR BOH (hammock)(cal days)	3	589*	11FEB08	21SEP09	11FEB08	21SEP09	0
ZZCA-0100	OVERALL DURATION FOR CASINO (hammock)(cal days)	3	589*	11FEB08	21SEP09	11FEB08	21SEP09	0
ZZPG-9995	PARKING GARAGE COMPLETE (finish milestone)	3	0		24OCT08		21SEP09	332
ZZSW-9995	SITEWORK COMPLETE (finish milestone)	3	0		31MAR09		21SEP09	174
ZZHT-9995	HOTEL TOWER COMPLETE (finish milestone)	3	0		12JUN09		21SEP09	101
ZZBH-9995	BACK OF HOUSE AREAS COMPLETE (finish milestone)	3	0		21SEP09		21SEP09	0
ZZCA-9995	TURNOVER 1 COMPLETE (finish milestone)	3	0		21SEP09		21SEP09	0
ZZZZ-9999	PROJECT COMPLETE (finish milestone)	3	0		21SEP09		21SEP09	0
SITEWORK ACTIVITIES								
SITEWORK								
SITEWORK ACTIVITIES								
SWNP-0200	ROUGH GRADE- NORTH PKG LOTS	1	5	24JUL08	30JUL08	19JUN09	26JUN09	213
SWVP-0200	ROUGH GRADE- VALET PKG/SO ACCESS	1	5	24JUL08	30JUL08	19JUN09	26JUN09	213
SWNP-0220	INSTALL UTILITIES - NORTH PKG LOTS	1	10	31JUL08	14AUG08	29JUN09	14JUL09	213
SWVP-0220	INSTALL UTILITIES - VALET PKG/SO ACCESS	1	10	31JUL08	14AUG08	29JUN09	14JUL09	213
SWSB-0200	ROUGH GRADE - SOUTH OF BLDG	1	5	08AUG08	14AUG08	05MAY09	11MAY09	173
SWNP-0230	GRADE/PLACE/FINISH CURB/GUTTER- NORTH PKG LOTS	1	5	15AUG08	22AUG08	15JUL09	21JUL09	213
SWVP-0230	GRADE/PL/FINISH CURB/GUTTER- VALET PKG/SO ACCESS	1	5	15AUG08	22AUG08	15JUL09	21JUL09	213
SWSB-0220	INSTALL UTILITIES - SOUTH OF BLDG	1	10	15AUG08	29AUG08	12MAY09	27MAY09	173
SWNP-0270	LAY ASPHALT PAVING - NORTH PKG LOTS	1	10	25AUG08	08SEP08	23JUL09	06AUG09	213
SWVP-0270	LAY ASPHALT PAVING - VALET PKG/SO ACCESS	1	10	25AUG08	08SEP08	23JUL09	06AUG09	213
SWSB-0230	GRADE/PLACE/FINISH CURB/GUTTER - SOUTH OF BLDG	1	15	02SEP08	23SEP08	28MAY09	18JUN09	173
SWNP-0290	INSTALL IRRIGATION/LANDSCAPE - NORTH PKG LOTS	1	15	09SEP08	30SEP08	07AUG09	28AUG09	213
SWVP-0290	IRRIGATION/LANDSCAPE - VALET PKG/SO ACCESS	1	15	09SEP08	30SEP08	07AUG09	28AUG09	213
SWSB-0250	FORM/PLACE/FINISH HARDSCAPE - SOUTH OF BLDG	1	20	09SEP08	07OCT08	04JUN09	06JUL09	173

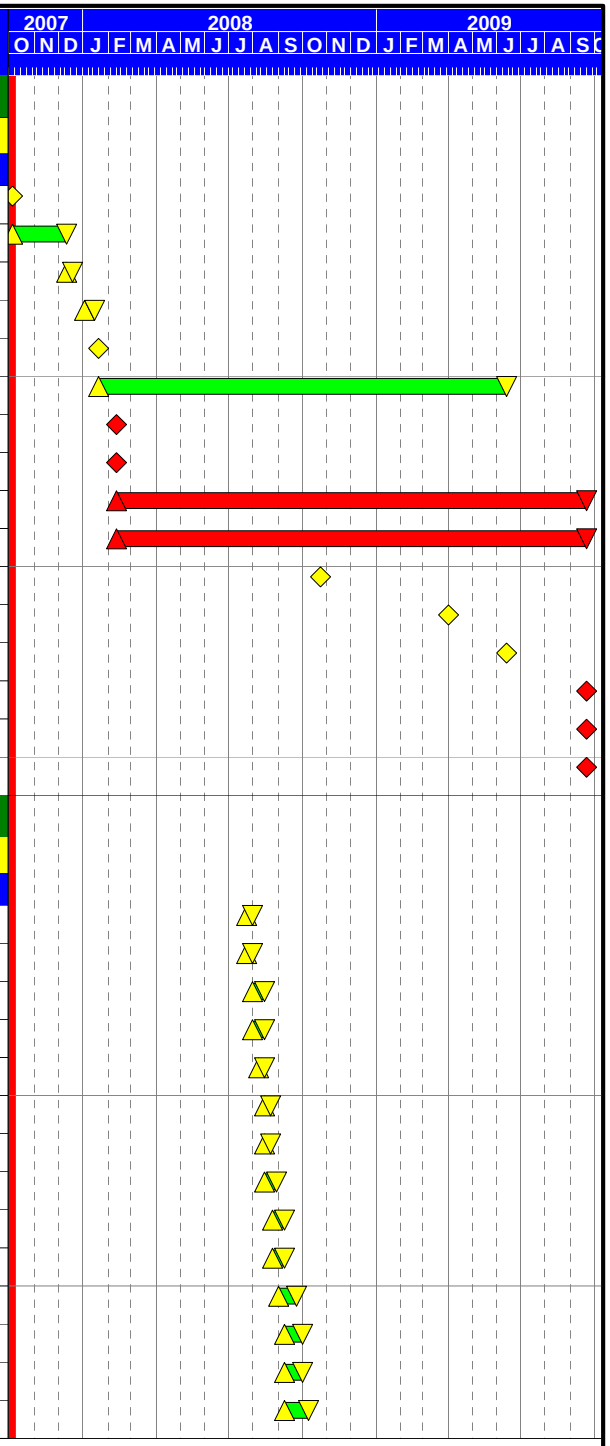

Start Date 05OCT07
Finish Date 21SEP09
Data Date 05OCT07
Run Date 29JAN08 13:43

© Primavera Systems, Inc.

WHP9

SCHEDULING CONSULTANTS, LTD.
PRELIMINARY SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA CODE

Date	Revision	Checked	Approved

Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
SITEWORK ACTIVITIES								
SWBO-0200	ROUGH GRADE- BUS/OVERFLOW PKG	1	10	01OCT08	14OCT08	20MAY09	03JUN09	148
SWNP-8880	PREPARE/COMPLETE PUNCHLIST - NORTH PKG LOTS	1	15	01OCT08	21OCT08	31AUG09	21SEP09	213
SWVP-8880	PREPARE/COMPLETE PUNCHLIST - VALET PKG/SO	1	15	01OCT08	21OCT08	31AUG09	21SEP09	213
SWLD-0200	ROUGH GRADE- LOAD DOCK/MECH YD	1	5	08OCT08	14OCT08	08JUN09	15JUN09	155
SWSB-0270	LAY ASPHALT PAVING - SOUTH OF BLDG	1	10	08OCT08	21OCT08	07JUL09	21JUL09	173
SWLD-0220	INSTALL UTILITIES - LOAD DOCK/MECH YD	1	10	15OCT08	29OCT08	16JUN09	30JUN09	155
SWBO-0220	INSTALL UTILITIES - BUS/OVERFLOW PKG	1	15	15OCT08	05NOV08	04JUN09	26JUN09	148
SWLD-0240	FORM/PL/FINISH EQUIP PADS - LOAD DOCK/MECH YD	1	10	30OCT08	13NOV08	07JUL09	21JUL09	158
SWLD-0230	GRADE/PLACE/FINISH CURB/GUTTER-LOAD DOCK/MECH	1	15	30OCT08	20NOV08	01JUL09	24JUL09	155
SWBO-0230	GRADE/PLACE/FINISH CURB/GUTTER- BUS/OVERFLOW	1	15	06NOV08	01DEC08	29JUN09	21JUL09	148
SWLD-1500	SET/CONNECT MECH/ELEC EQUIP - LOAD DOCK/MECH YD	1	25	14NOV08	23DEC08	23JUL09	28AUG09	158
SWLD-0270	FORM/PL/FINISH CONC PAVING - LOAD DOCK/MECH YD	1	8	21NOV08	04DEC08	27JUL09	06AUG09	155
SWBO-0270	BASE/ASPHALT PAVING - BUS/OVERFLOW PKG	1	10	02DEC08	16DEC08	23JUL09	06AUG09	148
SWLD-0255	ASHPALT PAVING/STRIPPING - LOAD DOCK/MECH YD	1	5	05DEC08	12DEC08	07AUG09	13AUG09	155
SWSB-0290	INSTALL IRRIGATION/LANDSCAPE - SOUTH OF BLDG	1	25	09DEC08	21JAN09	23JUL09	28AUG09	143
SWLD-0290	INSTALL IRRIGATION/LANDSCAPE - LOAD DOCK/MECH YD	1	10	15DEC08	02JAN09	14AUG09	28AUG09	155
SWNB-0200	GRADING FOR SITE CONCRETE - NORTH OF BLDG	1	5	29DEC08	06JAN09	19JUN09	26JUN09	113
SWLD-8880	PREPARE/COMPLETE PUNCHLIST - LOAD DOCK/MECH YD	1	15	05JAN09	26JAN09	31AUG09	21SEP09	155
SWNB-0230	FORM/PLACE/FINISH SITE CONCRETE - NORTH OF BLDG	1	20	07JAN09	05FEB09	29JUN09	29JUL09	113
SWSB-8880	PREPARE/COMPLETE PUNCHLIST - SOUTH OF BLDG	1	15	22JAN09	13FEB09	31AUG09	21SEP09	143
SWNB-0290	INSTALL IRRIGATION/LANDSCAPE - NORTH OF BLDG	1	20	06FEB09	09MAR09	30JUL09	28AUG09	113
SWBO-0290	INSTALL IRRIGATION/LANDSCAPE - BUS/OVERFLOW PKG	1	15	12FEB09	05MAR09	07AUG09	28AUG09	115
SWBO-8880	PREPARE/COMPLETE PUNCHLIST - BUS/OVERFLOW PKG	1	15	06MAR09	27MAR09	31AUG09	21SEP09	115
SWNB-8880	PREPARE/COMPLETE PUNCHLIST - NORTH OF BLDG	1	15	10MAR09	31MAR09	31AUG09	21SEP09	113
STRUCTURAL/ROOFING/EXTERIOR STUDS								
ACTIVITIES AFFECTING ALL FLOORS OF THE BUILDING								
PARKING GARAGE ACTIVITIES								
PGP1-0320	ERECT PRECAST CONCRETE - GRD LN B1-B3 - PG AF	1	25	23APR08	29MAY08	19MAR09	23APR09	211
PGP2-0320	ERECT PRECAST CONCRETE - GRD LN B3-B5 - PG AF	1	25	30MAY08	07JUL08	24APR09	01JUN09	211
PGAP-0550	INSTALL STAIRS/GUARD RLS - GRN LN B1-B5 - PG AF	1	15	08JUL08	30JUL08	30JUL09	21AUG09	248
BASEMENT LEVEL								
HOTEL TOWER ACTIVITIES								
HTBL-0237	DRILL/PLACE CAISSONS - HOTEL BSMT	1	5	21JAN08	25JAN08	16MAY08	22MAY08	79
HTBL-0322	FORM/PLACE CORE/SHEAR WALLS - HOTEL BSMT	1	10	24JAN08	06FEB08	21MAY08	04JUN08	79
HTBL-1500	R-I UNDERSLAB M.E.P. - HOTEL BSMT	1	5	11FEB08	18FEB08	30MAY08	05JUN08	73

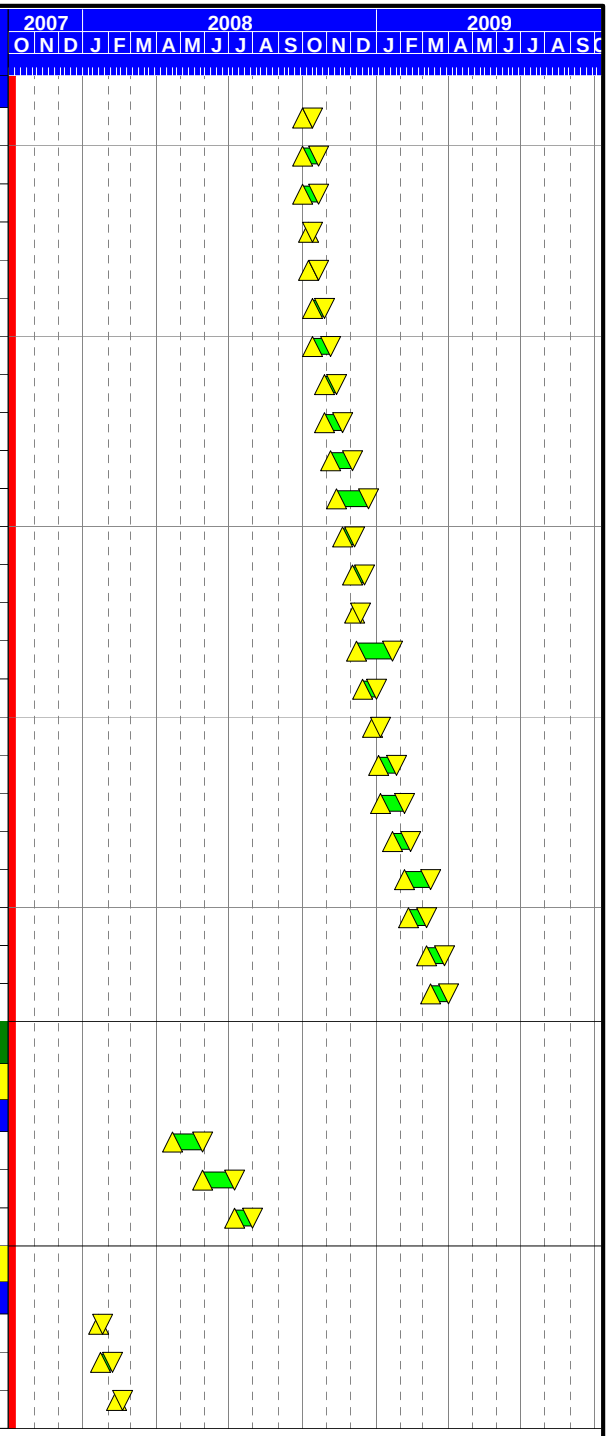

Start Date 05OCT07
Finish Date 21SEP09
Data Date 05OCT07
Run Date 29JAN08 13:43

© Primavera Systems, Inc.

WHP9

SCHEDULING CONSULTANTS, LTD.
PRELIMINARY SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA CODE

Date	Revision	Checked	Approved

Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
HOTEL TOWER ACTIVITIES								
HTBL-0380	FORM/PL/FINISH SLAB ON GRADE - HOTEL BSMT	1	4	19FEB08	25FEB08	06JUN08	12JUN08	73
HTBL-0222	BACKFILL FOUNDATIONS - HOTEL BSMT	1	3	04MAR08	06MAR08	20JUN08	24JUN08	73
BACK OF HOUSE AREA ACTIVITIES								
BHBL-1500	R-I UNDERSLAB M.E.P. - BOH TUNNELS BSMT	1	25	21JAN08	26FEB08	18APR08	23MAY08	60
BHBL-0310	FORM/PL SLAB ON GRADE (ftg) - BOH TUNNELS BSMT	1	25	30JAN08	06MAR08	29APR08	04JUN08	60
BHBL-0322	FORM/PLACE CORE/SHEAR WALLS - BOH TUNNELS BSMT	1	40	06FEB08	04APR08	06MAY08	03JUL08	60
BHBL-0222	BACKFILL FOUNDATIONS - BOH TUNNELS BSMT	1	30	05MAR08	17APR08	03JUN08	17JUL08	60
FLOOR ONE								
HOTEL TOWER ACTIVITIES								
HTF1-0237	DRILL/PLACE CAISSONS/GRADE BEAMS - HOTEL FL-1	1	25	11FEB08	19MAR08	19MAY08	24JUN08	65
HTF1-1500	R-I UNDERSLAB M.E.P. - HOTEL FL-1	1	25	19FEB08	26MAR08	30MAY08	07JUL08	68
HTF1-0350	FORM/PL/FINISH/STRIP DECK @ TUNNELS - HOTEL FL-1	1	5	26FEB08	03MAR08	13JUN08	19JUN08	73
HTF1-0360	FORM/PLACE COLUMNS/WALLS - HOTEL FL-1	1	15	10MAR08	31MAR08	16JUN08	07JUL08	65
HTF1-0380	FORM/PL/FINISH SLAB ON GRADE - HOTEL FL-1	1	15	18MAR08	07APR08	23JUN08	15JUL08	65
HTF1-0520	ERECT EXTERIOR STUDS - HOTEL FL-1	1	10	23APR08	06MAY08	21AUG08	04SEP08	78
BACK OF HOUSE AREA ACTIVITIES								
BHF1-0350	FORM/PL/FINISH/STRIP DECK @ TUNNELS - BOH FL-1	1	35	22FEB08	11APR08	21MAY08	14JUL08	60
BHF1-0310	FORM/PLACE FOOTINGS - BOH FL-1	1	35	05MAR08	24APR08	03JUN08	25JUL08	60
BHF1-1500	R-I UNDERSLAB M.E.P. - BOH FL-1	1	40	13MAR08	08MAY08	23JUN08	22AUG08	68
BHF1-0360	FORM/PLACE WALLS/PITS - BOH FL-1	1	20	01APR08	29APR08	30JUN08	30JUL08	60
BHF1-0380	FORM/PL/FINISH SLAB ON GRADE - BOH FL-1	1	35	08APR08	29MAY08	08JUL08	29AUG08	60
BHF1-0382	FORM/PL/FINISH SOG (crane access) - BOH FL-1	1	20	09SEP08	07OCT08	01OCT08	29OCT08	15
BHF1-0723	SPRAY-ON FIREPROOFING - BOH FL-1	1	25	17SEP08	21OCT08	08OCT08	13NOV08	15
CASINO AREA ACTIVITIES								
CAF1-0310	FORM/PLACE FOOTINGS - CASINO FL-1	1	35	11FEB08	02APR08	11FEB08	02APR08	0
CAF1-1500	R-I UNDERSLAB M.E.P. - CASINO FL-1	1	40	19FEB08	17APR08	25FEB08	22APR08	3
CAF1-0360	FORM/PLACE WALLS/PITS - CASINO FL-1	1	25	03MAR08	07APR08	03MAR08	07APR08	0
CAF1-0380	FORM/PL/FINISH SLAB ON GRADE - CASINO FL-1	1	35	10MAR08	29APR08	10MAR08	29APR08	0
PBF1-0205	EXCVT FOR FTGS - PED BRIDGE F1	1	2	01APR08	02APR08	09JUL09	10JUL09	299
PBF1-0215	FM/PL CONC FOOTINGS - PED BRIDGE F1	1	4	03APR08	08APR08	13JUL09	16JUL09	299
PBF1-0245	BACKFILL FTGS - PED BRIDGE F1	1	2	09APR08	10APR08	17JUL09	20JUL09	299
PBAF-0530	ERECT STR STL/MTL DCK/STRS(all flrs)- PED BRIDGE	1	10	30MAY08	13JUN08	21JUL09	04AUG09	267
PBF1-0380	FM/PL/FN SLAB ON GRADE - PED BRIDGE F1	1	3	16JUN08	18JUN08	11AUG09	13AUG09	270
PBAF-0555	INSTALL HAND RAILS (all floors) - PED BRIDGE	1	5	24JUN08	30JUN08	14AUG09	21AUG09	267
CEF1-1410	INSTALL ESCALATOR TRUSSES - CASINO ENTRY FL-1	2	10	30JUN08	14JUL08	18JUL08	31JUL08	13
CAF1-0382	FORM/PL/FINISH SOG (crane access) - CASINO FL-1	1	20	30JUN08	30JUL08	08APR09	06MAY09	180

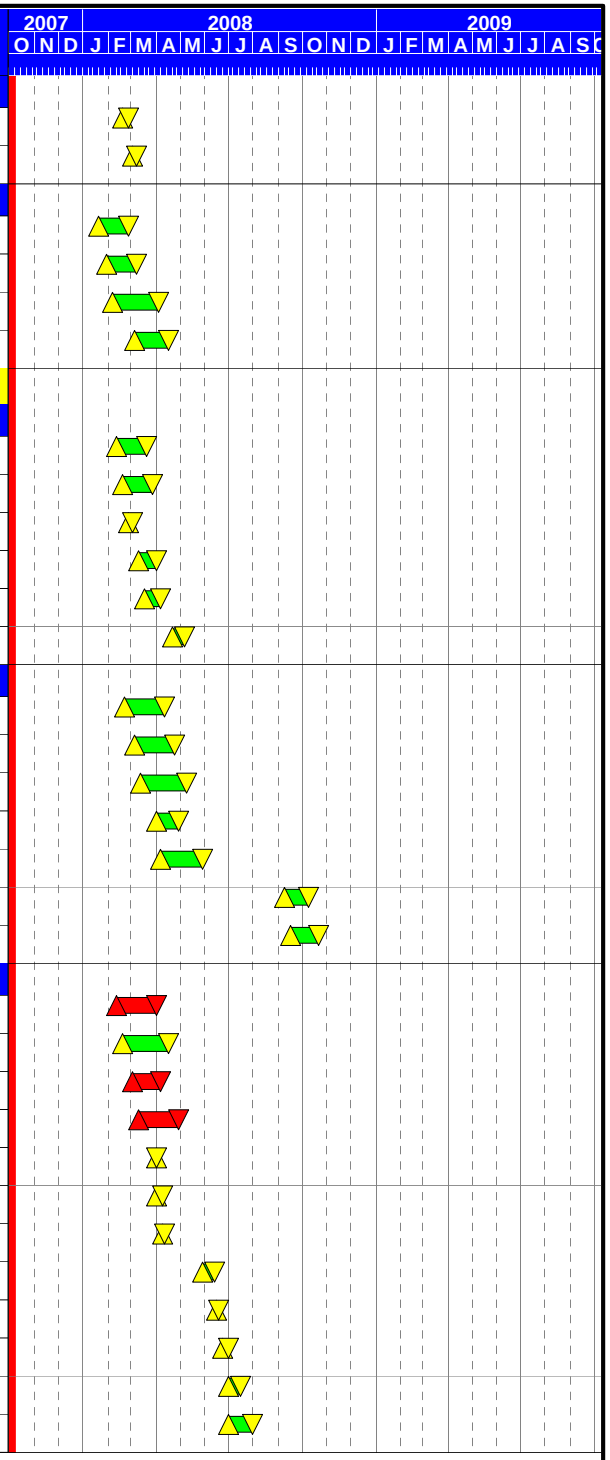

Start Date 05OCT07
Finish Date 21SEP09
Data Date 05OCT07
Run Date 29JAN08 13:43

© Primavera Systems, Inc.

WHP9

SCHEDULING CONSULTANTS, LTD.
PRELIMINARY SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA CODE

Date	Revision	Checked	Approved

Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
CASINO AREA ACTIVITIES								
CAF1-0723	SPRAY-ON FIREPROOFING - CASINO FL-1	1	15	16JUL08	07AUG08	16JUL08	07AUG08	0
PARKING GARAGE ACTIVITIES								
PGP1-0230	DRILL/PLACE CONC CASSIONS - GRD LN B1-B3 - PG F1	1	8	13MAR08	24MAR08	04FEB09	16FEB09	211
PGP1-0203	EXCAVATE FOR GRADE BEAMS - GRD LN B1-B3 - PG F1	1	5	25MAR08	31MAR08	17FEB09	24FEB09	211
PGP2-0230	DRILL/PLACE CONC CASSIONS - GRD LN B3-B5 - PG F1	1	8	25MAR08	03APR08	16MAR09	25MAR09	228
PGP1-0313	FORM/PL CONC GRADE BEAMS - GRD LN B1-B3 - PG F1	1	12	01APR08	17APR08	25FEB09	13MAR09	211
PGP2-0203	EXCAVATE FOR GRADE BEAMS - GRD LN B3-B5 - PG F1	1	5	04APR08	10APR08	26MAR09	01APR09	228
PGP2-0313	FORM/PL CONC GRADE BEAMS - GRD LN B3-B5 - PG F1	1	12	11APR08	29APR08	02APR09	17APR09	228
PGP1-0243	BACKFILL GRADE BEAMS - GRD LN B1-B3 - PG F1	1	3	18APR08	22APR08	16MAR09	18MAR09	211
PGP2-0243	BACKFILL GRADE BEAMS - GRD LN B3-B5 - PG F1	1	3	30APR08	02MAY08	20APR09	23APR09	228
PGP1-1505	R-I UNDERSLAB PLUMBING - GRD LN B1-B3 - PG F1	1	8	30MAY08	10JUN08	04JUN09	16JUN09	238
PGP2-1505	R-I UNDERSLAB PLUMBING - GRD LN B3-B5 - PG F1	1	10	08JUL08	22JUL08	02JUN09	16JUN09	211
PGAP-0380	FM/PL/FN SLAB ON GRADE - GRD LN B1-B5 - PG F1	1	12	24JUL08	11AUG08	17JUN09	06JUL09	211
FLOOR TWO								
HOTEL TOWER ACTIVITIES								
HTF2-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-2	1	15	01APR08	22APR08	08JUL08	30JUL08	65
HTF2-0520	ERECT EXTERIOR STUDS - HOTEL FL-2	1	10	07MAY08	21MAY08	05SEP08	19SEP08	78
BACK OF HOUSE AREA ACTIVITIES								
BHF2-0390	FORM/PL/FINISH TOPPING SLAB - BOH FL-2	1	25	02SEP08	07OCT08	24SEP08	29OCT08	15
BHF2-0392	FORM/PLACE/FINISH LIGHT WEIGHT CONC - BOH FL-2	1	15	17SEP08	07OCT08	15OCT08	05NOV08	20
BHF1-0540	ERECT EXT STUDS/SHTG FL-2 to ROOF - BOH FL-2	1	20	17SEP08	14OCT08	25NOV08	30DEC08	47
BHF2-0723	SPRAY-ON FIREPROOFING - BOH FL-2	1	15	24SEP08	14OCT08	23OCT08	13NOV08	20
BHF2-0750	APPLY ROOFING SYSTEM (low roof) - BOH ROOF FL-2	1	15	30OCT08	20NOV08	12DEC08	08JAN09	27
CASINO AREA ACTIVITIES								
CAF2-0390	FORM/PL/FINISH TOPPING SLABS - CASINO FL-2	1	45	22MAY08	30JUL08	22MAY08	30JUL08	0
CAF1-0540	ERECT EXT STUDS/SHTG (roof steps) - CASINO FL-2	1	15	06JUN08	27JUN08	25NOV08	18DEC08	112
PBF2-0327	FM/PL/FIN TOPPING SLAB - PED BRIDGE F2	1	2	16JUN08	17JUN08	06AUG09	07AUG09	267
CAF2-0723	SPRAY-ON FIREPROOFING - CASINO FL-2	1	15	31JUL08	22AUG08	26JAN09	17FEB09	112
PARKING GARAGE ACTIVITIES								
PGAP-0327	FM/PL/FIN TOPPING SLAB - GRD LN B1-B5 - PG F2	1	10	21JUL08	04AUG08	15JUN09	29JUN09	211
FLOOR THREE								
HOTEL TOWER ACTIVITIES								
HTF3-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-3	1	10	23APR08	06MAY08	13AUG08	27AUG08	73
HTF3-0520	ERECT EXTERIOR STUDS - HOTEL FL-3	1	10	15MAY08	29MAY08	15SEP08	26SEP08	78
CASINO AREA ACTIVITIES								
PBF3-0326	FM/PL/FIN TOPPING SLAB - PED BRIDGE F3	1	2	18JUN08	19JUN08	10AUG09	11AUG09	267

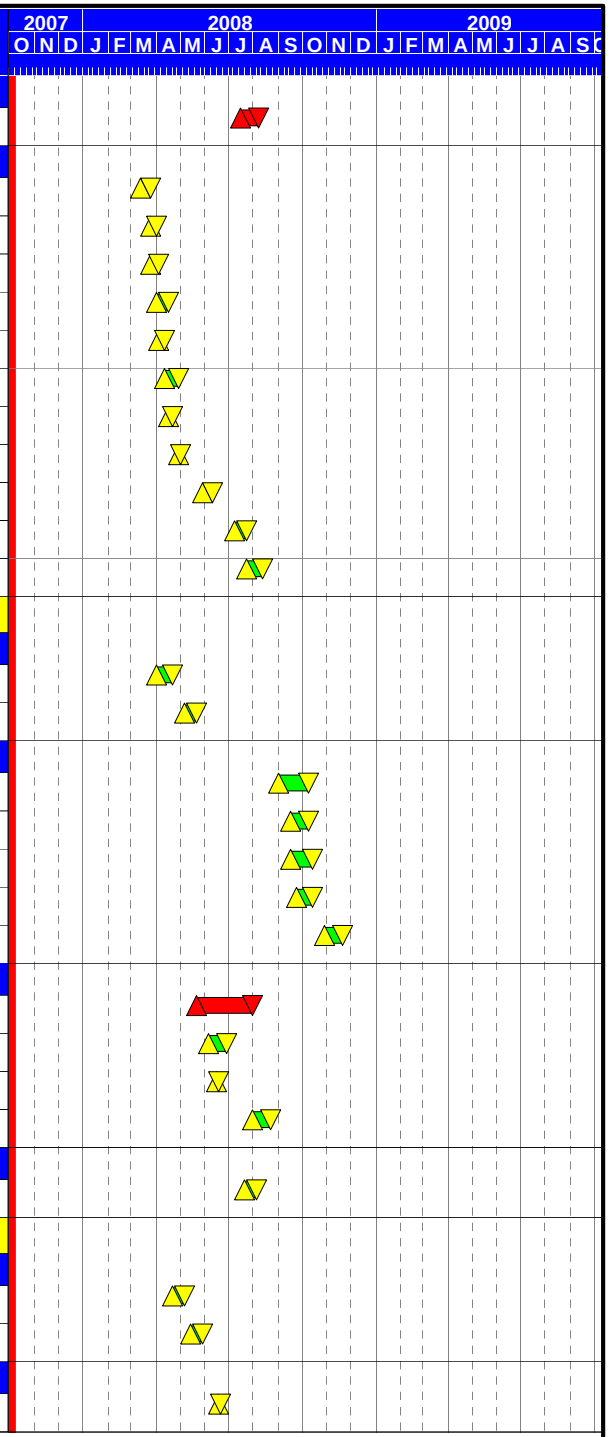

Start Date 05OCT07
Finish Date 21SEP09
Data Date 05OCT07
Run Date 29JAN08 13:43

© Primavera Systems, Inc.

WHP9

SCHEDULING CONSULTANTS, LTD.
PRELIMINARY SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA CODE

Date	Revision	Checked	Approved

Activity ID	Activity Description	Cal ID	Orig Dur	Early Start	Early Finish	Late Start	Late Finish	Total Float
PARKING GARAGE ACTIVITIES								
PGAP-0326	FM/PL/FIN TOPPING SLAB - GRD LN B1-B5 - PG F3	1	10	15JUL08	29JUL08	08JUN09	22JUN09	211
FLOOR FOUR								
HOTEL TOWER ACTIVITIES								
HTF4-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-4	1	10	30APR08	13MAY08	28AUG08	12SEP08	78
HTF4-0520	ERECT EXTERIOR STUDS - HOTEL FL-4	1	10	22MAY08	05JUN08	22SEP08	03OCT08	78
CASINO AREA ACTIVITIES								
PBF4-0325	FM/PL/FIN TOPPING SLAB - PED BRIDGE F4	1	2	20JUN08	23JUN08	12AUG09	13AUG09	267
PARKING GARAGE ACTIVITIES								
PGAP-0325	FM/PL/FIN TOPPING SLAB - GRD LN B1-B5 - PG F4	1	10	08JUL08	22JUL08	02JUN09	16JUN09	211
FLOOR FIVE								
HOTEL TOWER ACTIVITIES								
HTF5-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-5	1	10	07MAY08	21MAY08	05SEP08	19SEP08	78
HTF5-0520	ERECT EXTERIOR STUDS - HOTEL FL-5	1	10	30MAY08	13JUN08	29SEP08	10OCT08	78
FLOOR SIX								
HOTEL TOWER ACTIVITIES								
HTF6-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-6	1	10	15MAY08	29MAY08	15SEP08	26SEP08	78
HTF6-0520	ERECT EXTERIOR STUDS - HOTEL FL-6	1	10	06JUN08	20JUN08	06OCT08	17OCT08	78
FLOOR SEVEN								
HOTEL TOWER ACTIVITIES								
HTF7-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-7	1	10	22MAY08	05JUN08	22SEP08	03OCT08	78
HTF7-0520	ERECT EXTERIOR STUDS - HOTEL FL-7	1	10	16JUN08	27JUN08	13OCT08	27OCT08	78
FLOOR EIGHT								
HOTEL TOWER ACTIVITIES								
HTF8-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-8	1	10	30MAY08	13JUN08	29SEP08	10OCT08	78
HTF8-0520	ERECT EXTERIOR STUDS - HOTEL FL-8	1	10	23JUN08	07JUL08	20OCT08	03NOV08	78
FLOOR NINE								
HOTEL TOWER ACTIVITIES								
HTF9-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-9	1	10	06JUN08	20JUN08	06OCT08	17OCT08	78
HTF9-0520	ERECT EXTERIOR STUDS - HOTEL FL-9	1	10	30JUN08	15JUL08	28OCT08	10NOV08	78
FLOOR TEN								
HOTEL TOWER ACTIVITIES								
HTF0-0360	FORM/PL/FINISH PT DECK/COLS/WALLS - HOTEL FL-10	1	10	16JUN08	27JUN08	13OCT08	27OCT08	78
HTF0-0520	ERECT EXTERIOR STUDS - HOTEL FL-10	1	10	16JUL08	30JUL08	11NOV08	25NOV08	78
ROOF LEVEL								
HOTEL TOWER ACTIVITIES								
HTRL-0360	FORM/PL/FINISH PT DECK - HOTEL ROOF	1	15	23JUN08	15JUL08	20OCT08	10NOV08	78
HTRL-0512	ERECT STRUC STEEL/METAL DECK - HOTEL ROOF	1	15	16JUL08	07AUG08	21NOV08	16DEC08	85

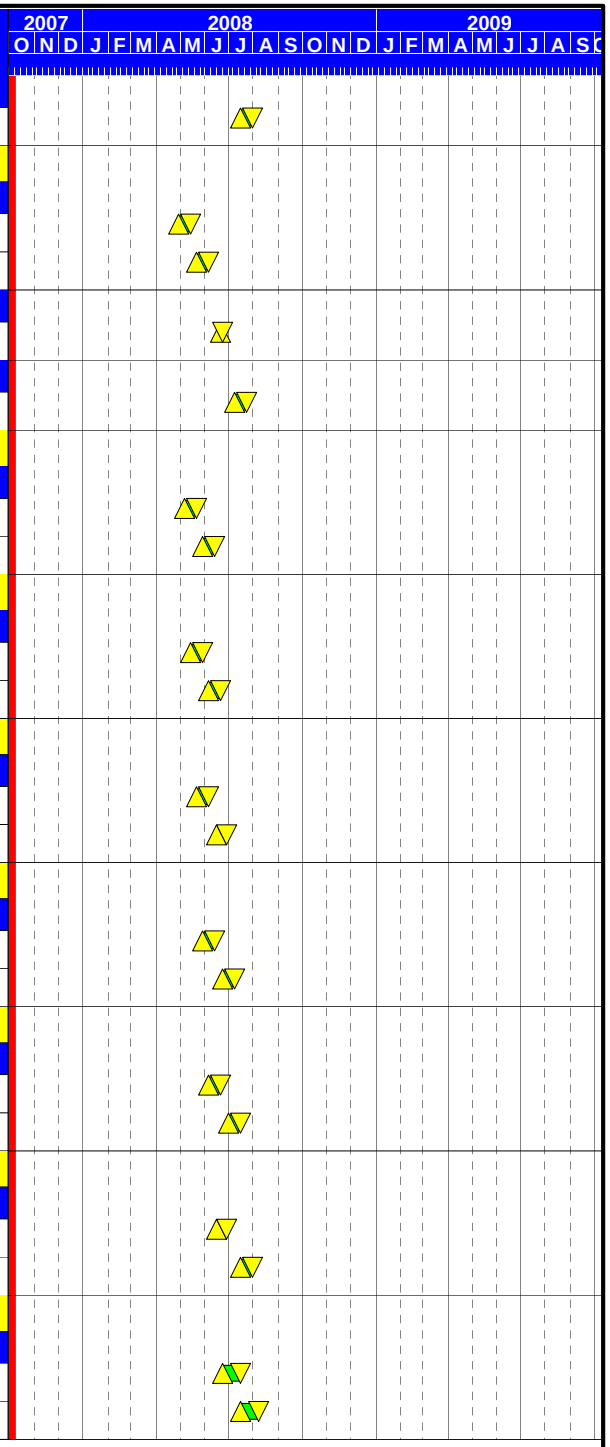

Start Date 05OCT07
Finish Date 21SEP09
Data Date 05OCT07
Run Date 29JAN08 13:43

© Primavera Systems, Inc.

WHP9

SCHEDULING CONSULTANTS, LTD.
PRELIMINARY SCHEDULE
ACTIVITIES GROUPED BY PHASE/LEVEL/AREA CODE

Date	Revision	Checked	Approved
